



Update:

Lockhart High School Additions & Renovations

Huckabee and OBR continue to meet with department heads and high school administration to develop the details of each area. Meetings with Food Service, CTE, and Technology have begun and details are being presented and comments incorporated during this Design Development phase. Each area is being asked to identify and provide information for their equipment needs or existing equipment that will be relocated.

The high school administration has formed a committee that has been working with the design architects to establish interior colors, materials and patterns that will be presented to the school board at the December meeting along with the Design Development package.

Huckabee consultants are preparing their documents for inclusion in the Design Development package including food service layout, structural and roofing plans. The exterior materials and details are being defined for presentation in December.

Bartlett-Cocke continues working on the details of the phasing and cost estimate for construction. The first construction item will be the asbestos abatement work during the December break, which will complete that scope in 3 of the classroom wings and counselor offices. This will enable us to begin construction immediately after school ends in 2015.

Rendering of Proposed New LHS Entry






Rendering of Performing Arts Center Entry



Lockhart High School Design Phase Timeline

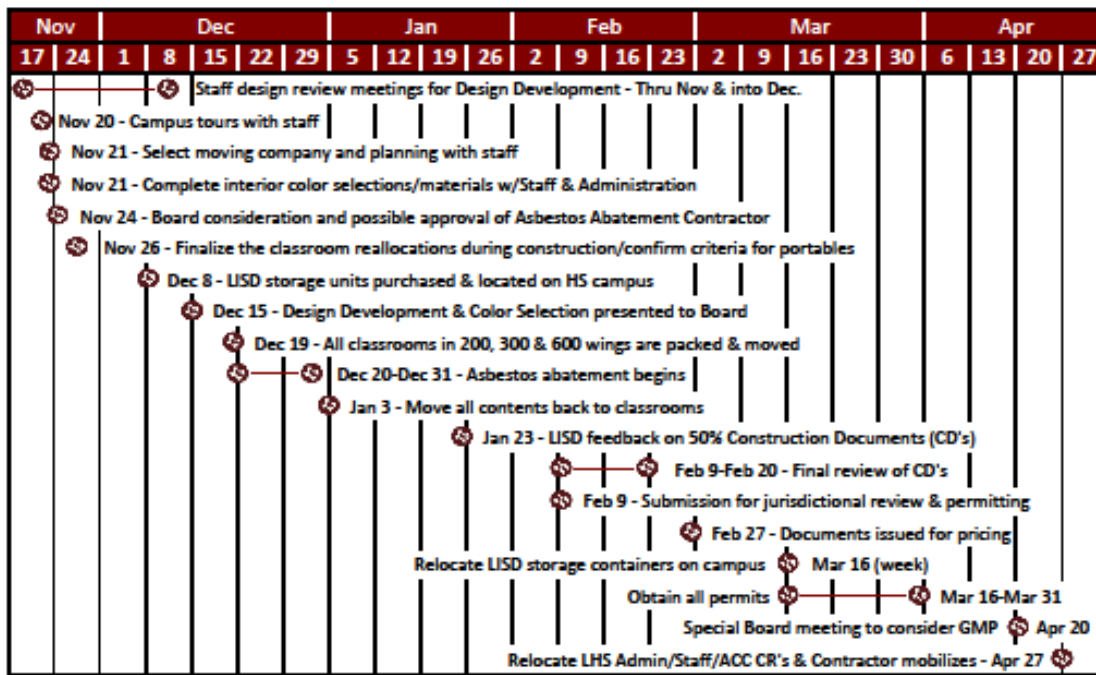

New Elementary School

The district has located the site for the new elementary and negotiations with the current owner have begun. Once contract negotiations have completed, then due diligence efforts will begin.

The first “visioning” meeting was held with numerous staff from all campuses. The definition of what education should look like in the future, along with categorizing “the good, the bad and the ugly” were part of the conceptual approach. The next step will be the touring of new area campus’s to see how they are handling instructional spaces and technology.

The Board will be presented with a progress report on “visioning” at the November 24, 2014 meeting.

District Wide Capital Improvements

Huckabee has begun schematic design documents for the improvements at Clear Fork Elementary and the asbestos consultant will begin testing/sampling of materials in the area to identify any abatement scope of work prior to construction. On the AC improvements for the elementary gymnasiums, an RFQ will be advertised to select a mechanical engineer for the design and construction documents. A civil engineer will be contracted for improvements at Carver Kindergarten for the new traffic loop and parking.

Looking Ahead:

- **November 20** – Tour of area elementary and high school campus’s
- **November 21** – Interior Design meetings for LHS color, material, and pattern selections
- **November 24** – Board meeting. Consideration/approval of ACM abatement contractor
- **December 2** – New Elementary Visioning meeting with principals
- **December 15** – Board meeting. Presentation of Design Development documents and LHS color schemes.
- **December 19 – January 3** – Relocation of LHS classroom furniture and ACM abatement phase 1.
